


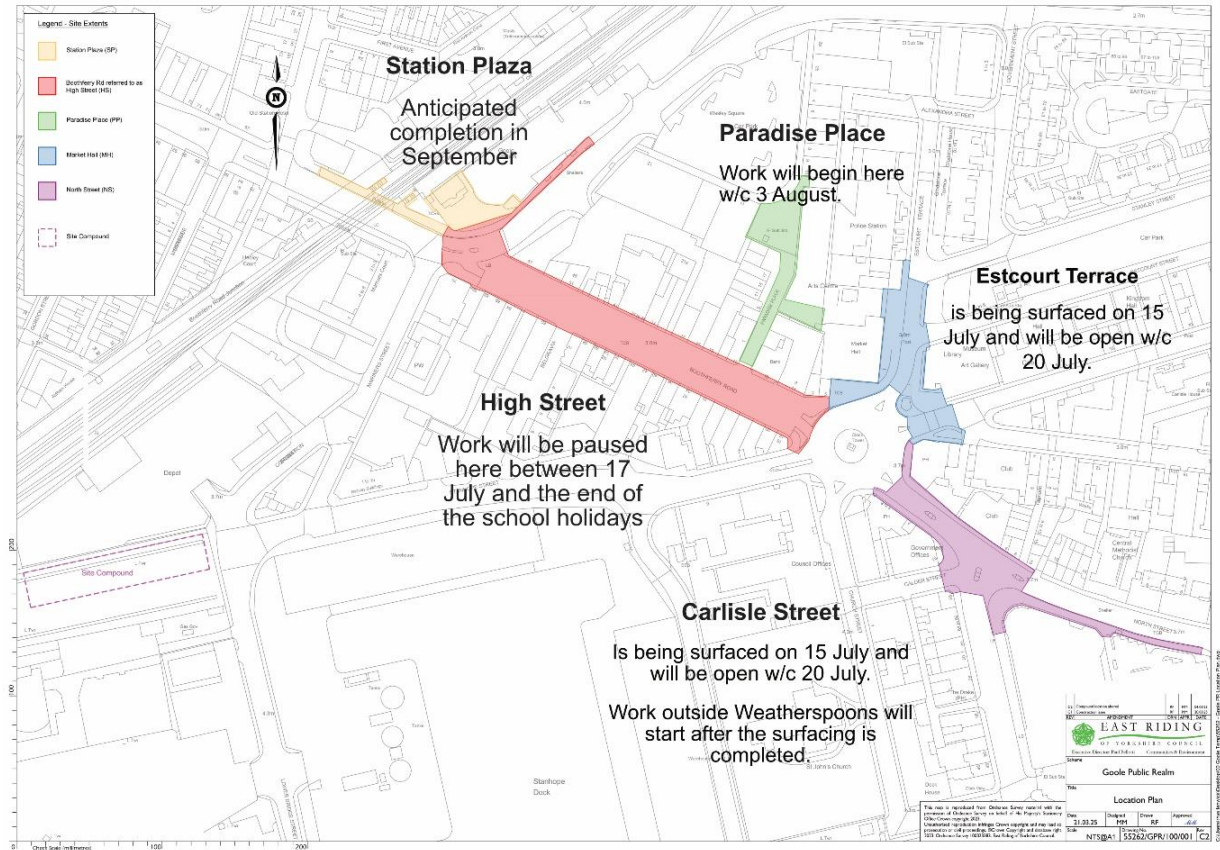

North Street

As stated in our last newsletter, we will be starting the minor remedial works to the area on Mid to late August for an anticipated duration of 2 days.

These final improvement works will ensure the scheme achieves the high-quality finish expected and provides long-term durability for residents, businesses and visitors.

Estcourt Terrace

Works outside the library have progressed well and remain on schedule for completion mid to late July.

The road closure for Estcourt Terrace is anticipated to be removed 17/07/2026

Works outside Wetherspoons will continue until mid to late August and we are working closely with the business to ensure access is maintained at all times.

We will return to the area outside the Market Hall in September to complete the final landscaping and paving elements of the scheme.

High Street

Significant progress continues to be made on High Street, with a number of new planters being completed, paving works advancing, and the installation of a feature bench and bespoke art screens helping to shape the area's new appearance.

As previously announced, Public Realm works on High Street will pause from 17 July. This break has been planned to provide businesses with a period free from construction activity and to allow residents and visitors to fully enjoy Goole's bicentenary celebrations during the summer. Works will resume in September and the High Street improvements remain on track for completion in Autumn 2026.

Yorkshire Water has notified us that it intends to carry out paving reinstatement works from 3 August following emergency repairs undertaken earlier this year. These works are separate from the Goole Public Realm Scheme but are necessary to ensure the paving meets the required standards and complements the wider improvements being delivered along High Street.

We are also awaiting confirmation from Yorkshire Water regarding the installation of a new water connection for the proposed water feature. Our preference is for these works to take place after Public Realm activities resume in September; however, Yorkshire Water's programme is managed independently. We will provide further updates as soon as information becomes available.

Paradise Place

Works at Paradise Place are scheduled to begin during the week commencing 3 August. The pattern of work remains the same as explained to businesses previously and is anticipated to be complete in Autumn 2026. Our Public Liaison Officer will re-visit Paradise Place businesses before works begin.

Station Plaza

Works outside Goole railway station continue to progress well and remain on programme for completion by the end of the summer.

Thank you for your continued patience and support while these improvements are delivered. We appreciate that construction works can cause temporary inconvenience, but the completed Public Realm Scheme will provide a more attractive, accessible and welcoming town centre for residents, businesses and visitors alike.

Breheny Civil Engineering Ltd: Public Liaison Officer (PLO) Neil Hallam

Email GoolePRS@breheny.co.uk

Tel / WhatsApp 07814 804 346

Web Updates www.gooletowndeal.co.uk/projects/public-realm/
